


Utah Stewardship Dashboard Environment


Meeting or Exceeding Targets 6 out of 8 Quarters in the Past 2 Years. (70-80%)

EISs Ahead and Behind Schedule

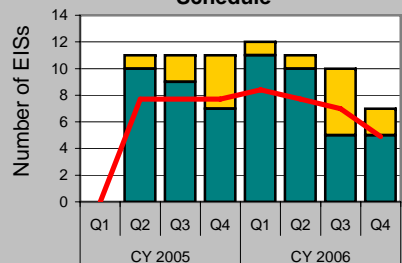


On Time	na	10	9	7	11	10	5	
Behind	na	1	2	4	1	1	2	
Percent	###	91	82	64	92	91	50	71 %
Target		70	70	70	70	70	70	70 %
	###	7.7	7.7	7.7	8.4	7.7	7	4.9
		1	1	0	1	1	0	1 0.7

EAs Ahead and Behind Schedule

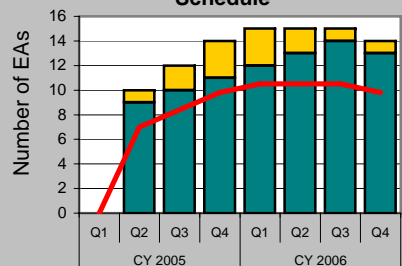


On Time	na	9	10	11	12	13	14	13
Behind	na	1	2	3	3	2	1	1
Percent	###	90	83	79	80	87	93	93 %
Target		70	70	70	70	70	70	70 %
	###	7	8.4	9.8	11	11	11	9.8
		1	1	1	1	1	1	1 1.0


EIS Median Timeframes

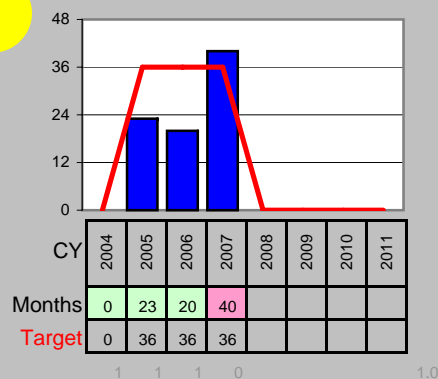


EA Median Timeframes

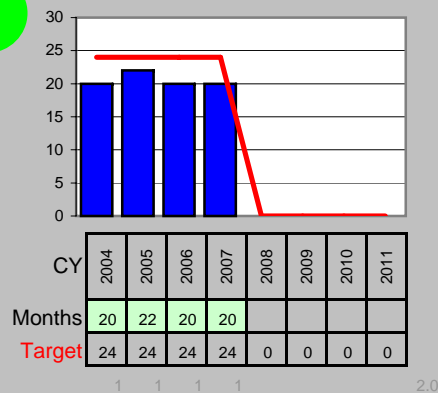


Number of Projs w/ DeMinimis

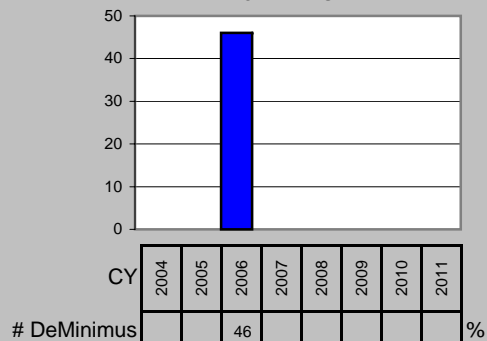


of EISs Complete

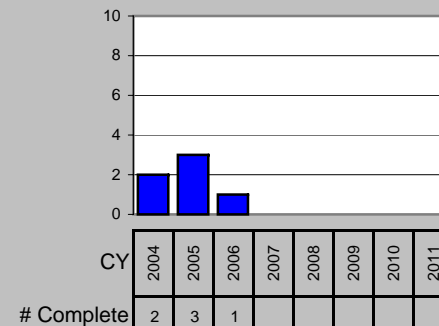

of EAs Complete

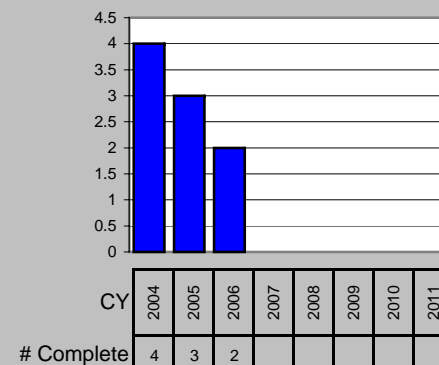

of CEs Complete

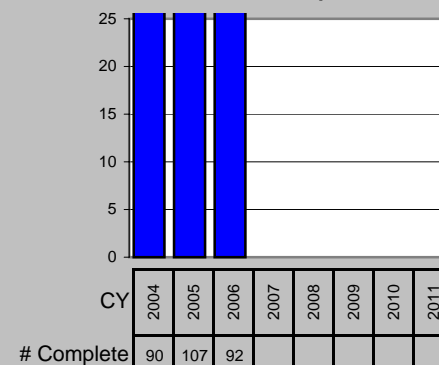






Utah Stewardship Dashboard

Environment - Page 2 - Measurement Descriptions




Schedule Indicators

(Represent performance over the last 8 quarters.)

-  Meeting or Exceeding Targets Every Quarter in the Last 2 Years (90%+)
-  Meeting or Exceeding Targets in 7 out of 8 Quarters in the Past 2 Years. (80-90%)
-  Meeting or Exceeding Targets 6 out of 8 Quarters in the Past 2 Years. (70-80%)
-  Meeting or Exceeding Targets 5 out of 8 Quarters in the Past 2 Years (60-70%)
-  Meeting or Exceeding Targets fewer than 5 of 8 Quarters in the Past 2 Years (<60%)

Timeframe Indicators

(Represent performance over previous 2 years)

-  Meeting Targets for Previous 2 Years
-  Meeting Targets 1 out of the Previous 2 Years
-  Not Meeting Targets in Either of the Previous 2 Years

EISs Ahead and Behind Schedule

Measure Description: Prior to beginning an Environmental Impact Statement (EIS), a schedule with milestones are negotiated. If the project milestones are reached on time then the project is on time or ahead of schedule (blue-green bar). Projects behind schedule are shown in gold.

Target Line: UDOT and FHWA-UT have set a goal to have 70% of all EISs proceeding on schedule. This is the quarterly target shown by a red line on the chart. It varies based on the number of EISs in progress.

Red & Pink Boxes: Another way of showing whether the targets were met for that quarter.

EAs Ahead and Behind Schedule

Measure Description: Prior to beginning an Environmental Assessment (EA), a schedule with milestones are negotiated. If the project milestones are reached on time then the project is on time or ahead of schedule (blue-green bar). Projects behind schedule are shown in gold.

Target Line: UDOT and FHWA-UT have set a goal to have 70% of all EISs proceeding on schedule. This is the quarterly target shown by a red line on the chart. It varies based on the number of EAs in progress.

Red & Pink Boxes: Another way of showing whether the targets were met for that quarter.

EIS Median Timeframes

Description: For all the EISs completed in a given year, this is the median number of months it took to complete the projects (NOI to ROD).

EA Median Timeframes

Description: For all the EAs completed in a given year, this is the median number of months it took to complete the projects (NOI to FONSI). (Utah has chosen to issue a NOI to mark the beginning of EAs.)

of EISs Complete

Description: This shows how many EISs have been completed in a given year.

of EAs Complete

Description: This shows how many EAs have been completed in a given year.

of Projects with De Minimis

Description: The total number of EISs, EAs, and CEs that have utilized the SAFETEA-LU De Minimis provision.

of CEs Complete

Description: This shows how many CEs have been completed in a given year.
